

CIP # 15-002 - Oneida Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:


- New wells have been installed.
 - ◊ Water testing of new wells has determined extra conditioning needs to take place. Design is being revised to accommodate added equipment.
- The pumphouse and water main extension are currently being designed by Indian Health Service (IHS).
 - ◊ After a tour of a similar facility, it has been decided to revise the design to provide better functionality.

Schedule:

Approvals - complete.
 Design - IHS anticipates completion of design in fall 2023.
 Bidding - 2023
 Construction - 2024-2025
 Substantial Completion - 2025

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

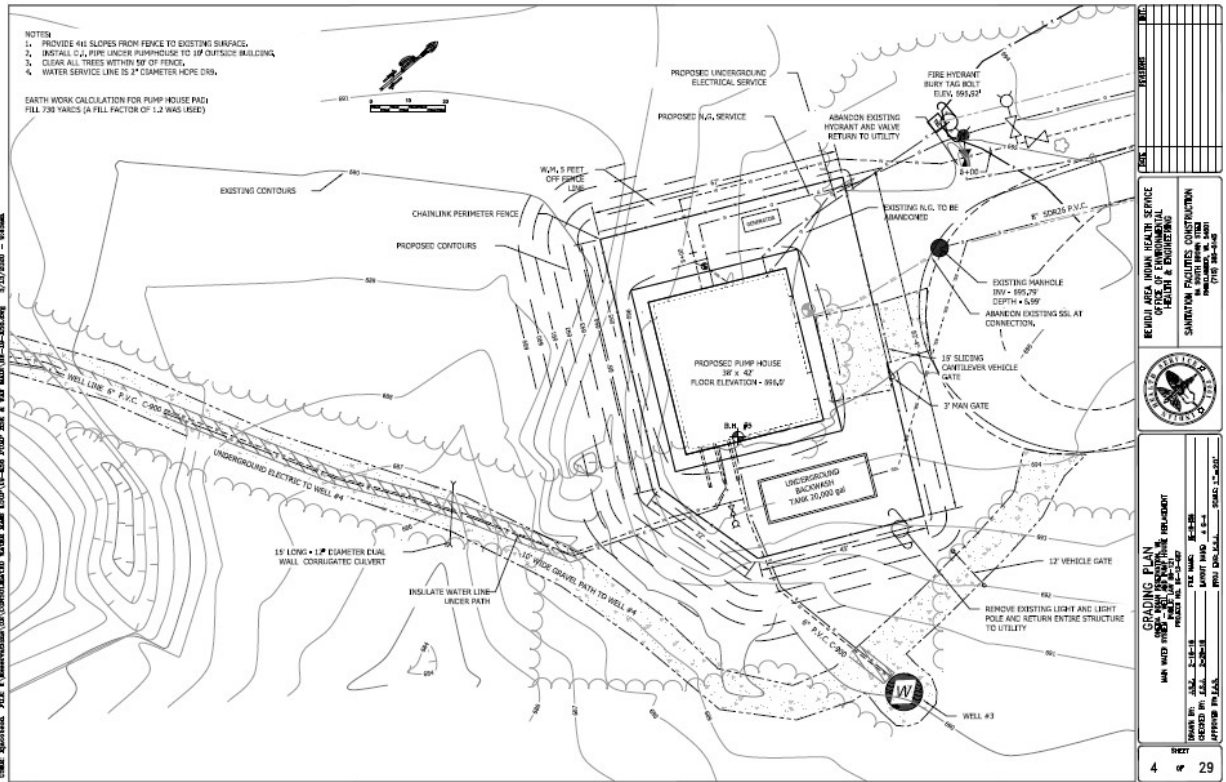

DESIGNER	
CHECKED	
REVISIONS	
REVISION NO.	DESCRIPTION
1	
2	
3	
4	
5	
6	
7	
8	
9	
10	
11	
12	
13	
14	
15	
16	
17	
18	
19	
20	
21	
22	
23	
24	
25	
26	
27	
28	
29	
30	
31	
32	
33	
34	
35	
36	
37	
38	
39	
40	
41	
42	
43	
44	
45	
46	
47	
48	
49	
50	
51	
52	
53	
54	
55	
56	
57	
58	
59	
60	
61	
62	
63	
64	
65	
66	
67	
68	
69	
70	
71	
72	
73	
74	
75	
76	
77	
78	
79	
80	
81	
82	
83	
84	
85	
86	
87	
88	
89	
90	
91	
92	
93	
94	
95	
96	
97	
98	
99	
100	
