CIP # 16-008 O.F.F. Facility Improvements

Project Description:

The proposed project will be completed in phases and will address the current facility deficiencies. The project will upgrade heating, ventilation and air conditioning in the gymnasium, spin rooms, and toilet rooms. Finish materials in the impacted spaces will be replaced as required. In addition, the men's and women's locker/shower rooms will be aligned for sizing needs of client demographic.

Current Status:

The upgrades to the heating, ventilation and air conditioning in the gymnasium, spin roomsm and toilet rooms are 80% complete.

Demo of the locker rooms is currently taking place over next two weeks.

Schedule:

Approvals - Complete

Design - Complete


Bidding - Complete

Construction - Underway

Substantial Completion - May of 2020

Project Partners:

Engineering Dept. Fitness Center Staff, DPW.

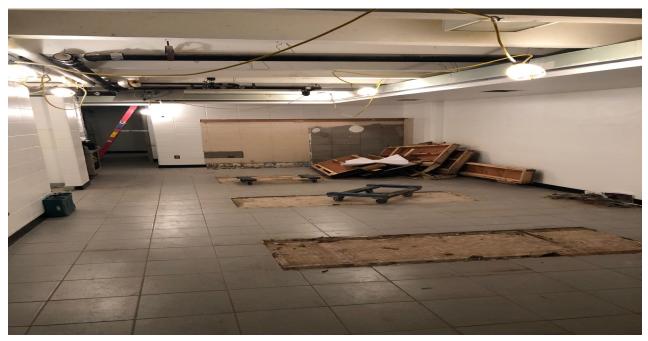

Date: 11/15/19



Engineering
