CIP # 15-002 - Oneida Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- New wells have been installed.
- The pumphouse and water main extension are currently being designed by Indian Health Service (IHS).
- Team working on getting utility service line agreements in place for the project.

Schedule:

Approvals - complete.

Design - IHS anticipates completion of design in May 2022.


Bidding - 2022

Construction - 2022-2023

Substantial Completion - 2023

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

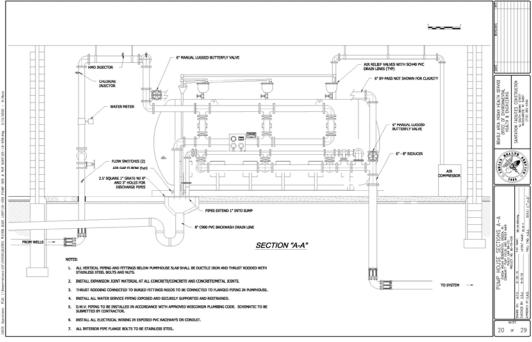

Date: 4/26/22

