

CIP # 07-002 SS Building Remodel Phase V

Project Description:

The approved project is a continuation of the various remodeling/upgrades of the existing facility. The project will address, in stages: building code, life safety, asbestos abatement, functional issues and operational inefficiencies. The project outcome will be an energy efficient, functional, healthy, safe and comfortable environment for the Social Services Building occupants and clients. The current stage of this phased remodeling project will focus on building HVAC upgrades.

Current Status:

Stage 3—HVAC: Construction prep work has started, Tweet Garot is installing Refrigerant line sets and electrical as well as both Wall and Ceiling Air Handling units in the West Wing and work is approximately 80% completed. Additionally, Tweet Garot is also updating existing hot water registers throughout with state of the art electronic control valves that will increase efficiency and room comfort. Once West Wing is completed work will progress to 2nd floor B-Wing. Rooftop Units are being lifted and placed onto roof.

Schedule:


1st FL WEST TURVH 144

1st FL SECTION B TURVH 096

1st FL EAST TURVH 240

1st FL SOUTH WEST TURVH 144

1st FL SECTION B TURVH 192

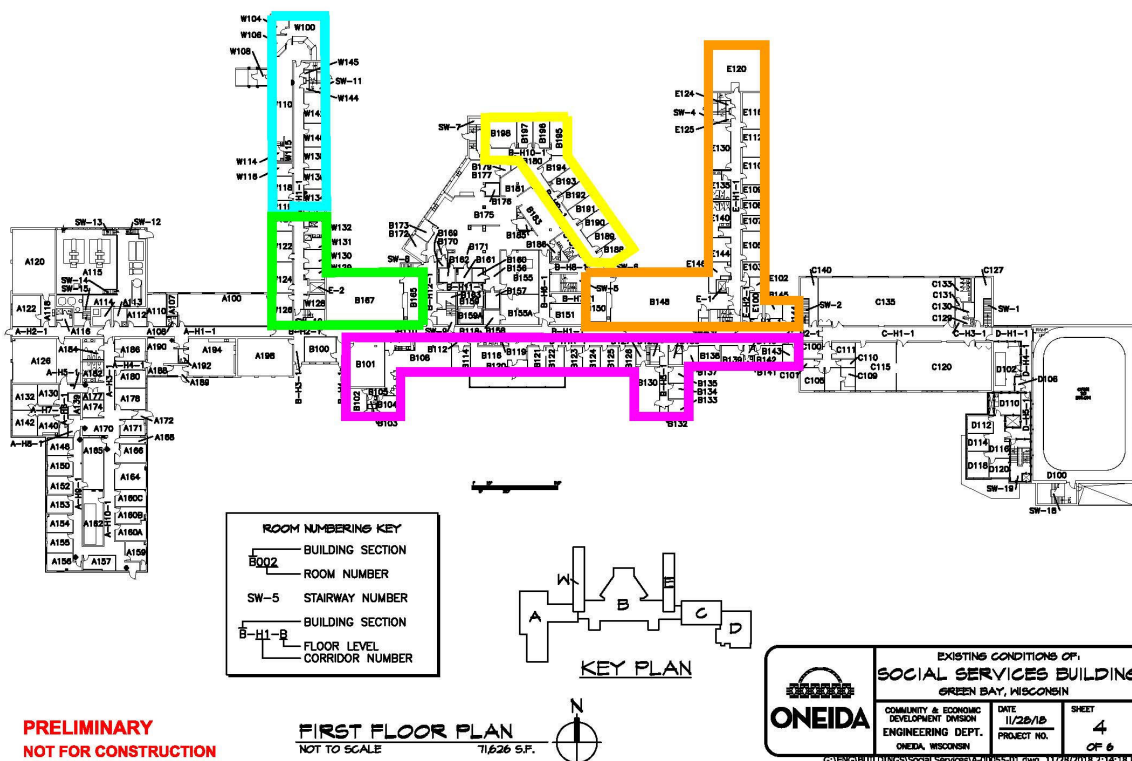

**STATUS
REPORT**

SS Building Remodel Phase V

CIP # 07-002 SS Building Remodel HVAC 3



ONEIDA

Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 10/29/22
