

CIP # 15-003 - NHC Remodeling—Phase VIII—Stage 4a

Project Description:

The approved project is a continuation of the various remodeling/upgrades of the existing facility. Stage 4a of the project will entail the remodeling of a portion of the first floor to create a reception area for the business office. It will separate the reception area for the high school from the reception area for the business functions within the building, thus improving security concerns with the current combined reception areas.

Current Status:


- MS2 is working Final Finishes
- MS2 is awaiting Reception desk Glass divider installation
- Steel Case Furnishings are installed
- Doors to be re-keyed by Boss Keys
- Printer to be re-located once electrical and data re-configured.

Schedule:

Approvals - complete.
Design - 2022
Bidding - 2022
Construction - 2022
Substantial Completion - 2022

Project Partners:

BC Support Office, High School, Engineering, DPW, DTS.

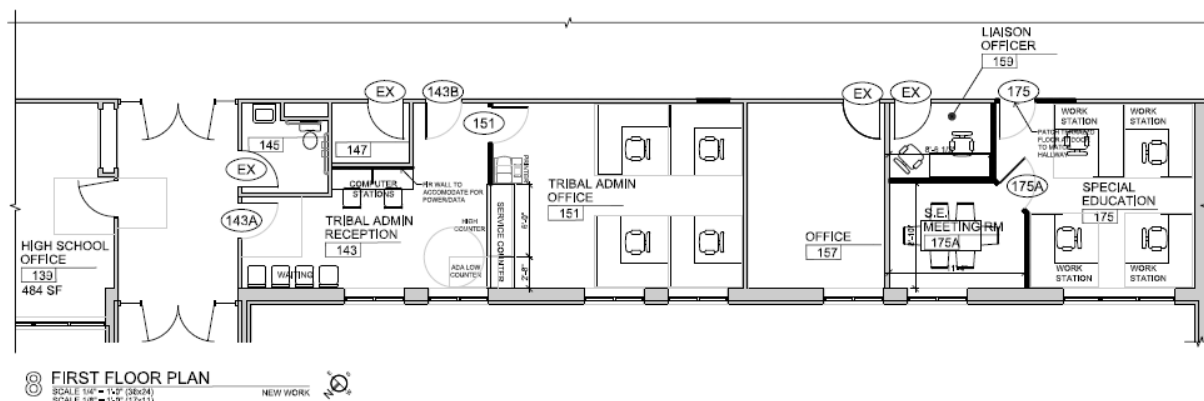

**STATUS
REPORT**

NHC Remodeling—Phase VIII

CIP # 15-003 - NHC Remodeling—Phase VIII—Stage 4a

