

ENG# 22-106 - Elder Village Cottages Phase IV

Project Description:

The project will construct 6 additional one and two bedroom homes in the Elder Village Neighborhood (Henry Road & Maria Hinton Way). The current phase has three different designs identified as “N-2”, “O-2”, and “P-2”. The 6 homes consist of: 3 of the N-2 Plan (1-bedroom), 1 of the O-2 plan (2-bedroom), and 2 of the P-2 plan (2-bedroom). The rental houses are reserved for Elders (62+) and will be administered by Comprehensive Housing Division.

Current Status:


Six foundations have been completed, with the framing of the houses starting September 2022. Project will complete the infill of the available infrastructure.

Schedule:

- Approvals - Complete
- Design - Complete
- Bidding - Complete—May 2022
- Construction - Spring 2023
- Estimated Substantial Completion—TBD

Project Partners:

Comprehensive Housing, Engineering, Planning, & DPW-Plumbing

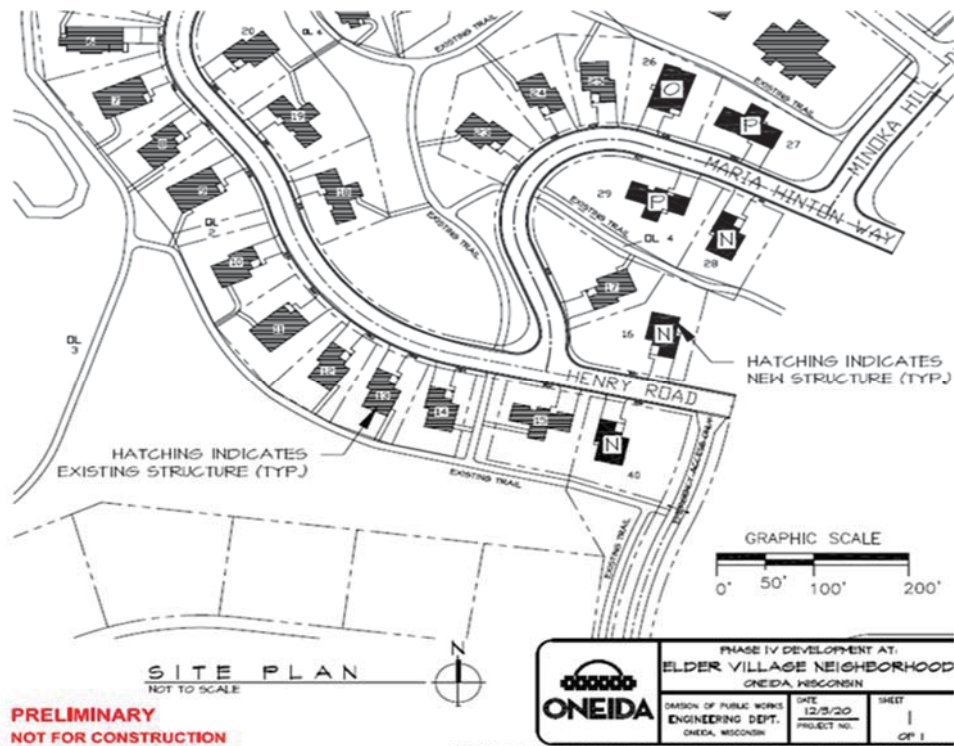

Engineering
Department

STATUS
REPORT

Elder Village Cottages - Phase IV

ENG# 22-106 - Elder Village Cottages Phase IV

Lot 40



Lot 16



Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 10/31/22

STATUS
REPORT

Elder Village Cottages - Phase IV

ENG# 22-106 - Elder Village Cottages Phase IV

Lot 28



Lot 29

