

## ENG # 22-102 - Ridgeland Community Water System Improvements

### Project Description:

The project will install a new well and extend the depth of one of the existing wells to improve the water system serving the Ridgeland Community area homes. The design documents are being prepared by Indian Health Service (IHS).

### Current Status:


- CTW Corporation is the awarded contractor.
- Well drilling has been completed.
- IHS reviewing results of well testing.

### Schedule:

Approvals - complete.  
 Design - complete.  
 Bidding - complete.  
 Construction - January 2023 - April 2023  
 Substantial Completion - March 2023

### Project Partners:

Utilities Dept., Engineering, IHS

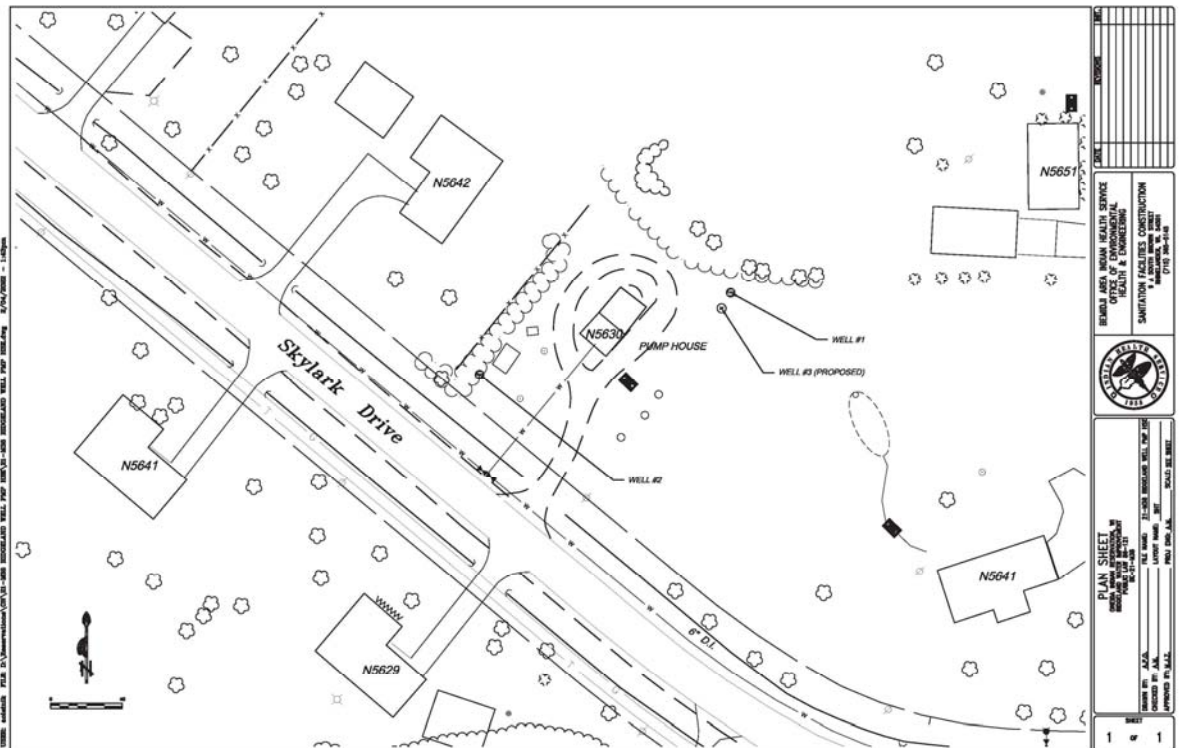

Engineering Department
