

## CIP # 15-002 - Oneida Community Wells

### Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

### Current Status:

- ◇ Phase One - Installation of new wells is complete
- ◇ Phase Two - Watermain work has been awarded with construction scheduled to begin in summer of 2025.
- ◇ Phase Three - Pumphouse bids due back in July.

### Schedule:

Approvals - complete.

Design - complete


Bidding - 2025

Construction - 2025 & 2026


Substantial Completion - 2027

### Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

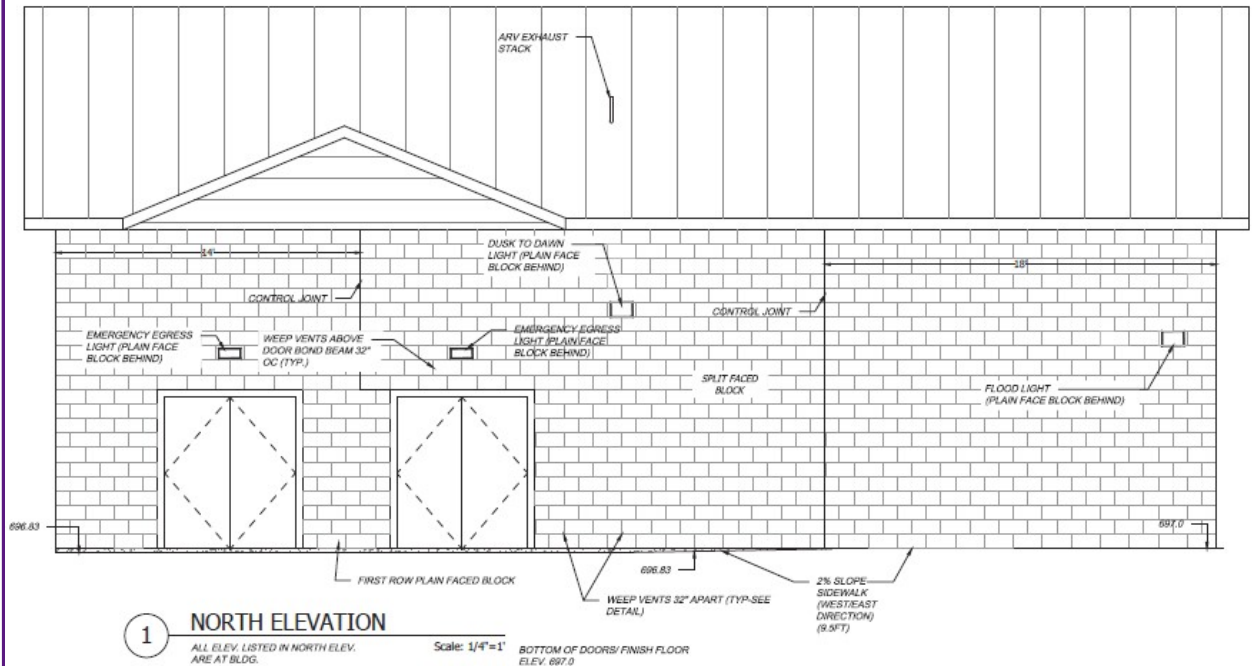

# Oneida Community Wells

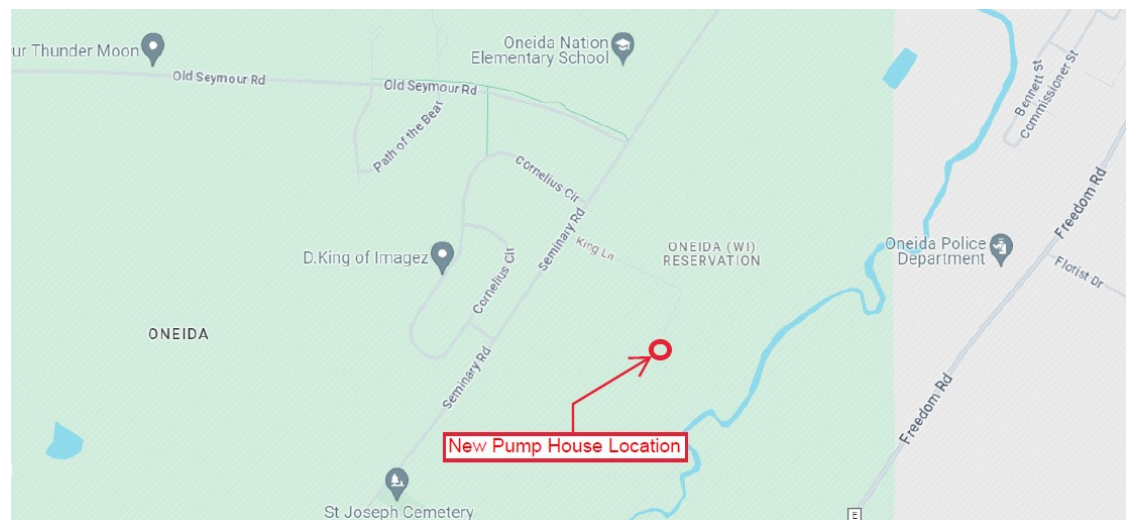[illegible]

Engineering  
Department

**Date: 6/5/2025**
