

CIP # 15-002 - Oneida Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- ◇ Phase One - Installation of new wells is complete
- ◇ Phase Two - Watermain work has begun from King Lane to County Rd E.
- ◇ Phase Three - Pumphouse bids were received. IHS and Engineering is in process of qualifying bids.

Schedule:

Approvals - complete.

Design - complete


Bidding - 2025

Construction - 2025 & 2026

Substantial Completion - 2027

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

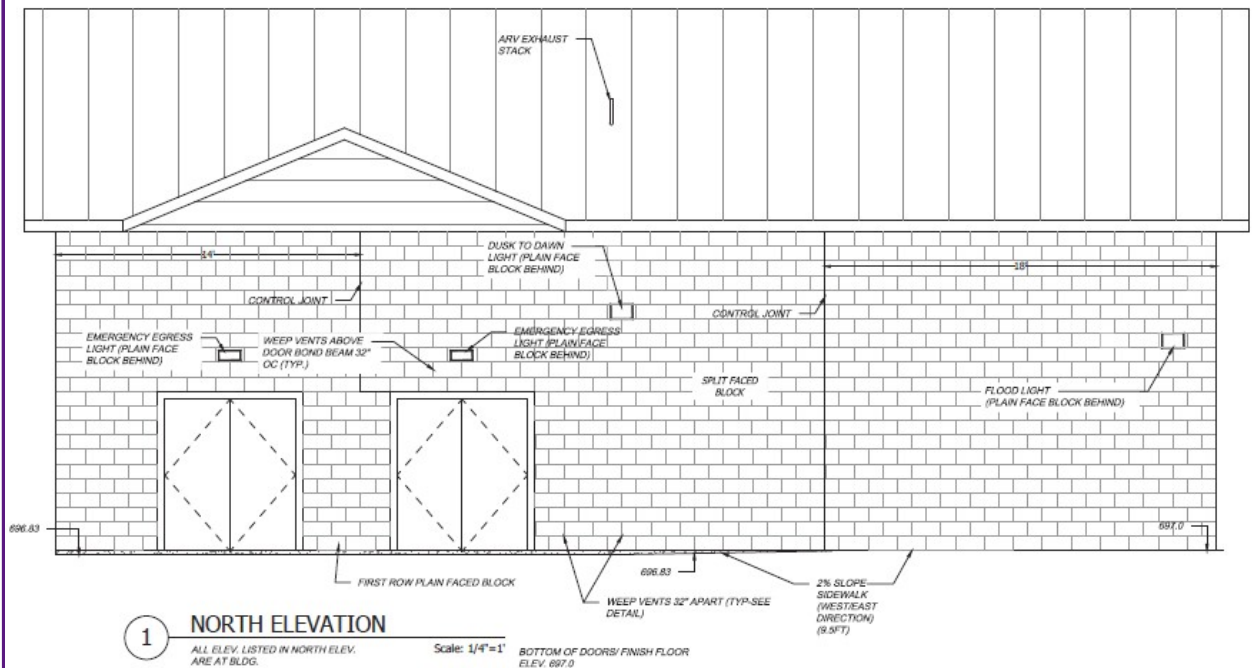

STATUS
REPORT

Oneida Community Wells

CIP # 15-002 - Oneida Community Wells



**STATUS
REPORT**

Oneida Community Wells

CIP # 15-002 - Oneida Community Wells



ONEIDA

Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 8/4/2025
