

CIP # 15-002 - King Lane Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:


- ◇ Phase One - Installation of new wells is complete
- ◇ Phase Two - Watermain loop from King Lane to County Road E is complete.
- ◇ Phase Three - New pump house site clearing complete with construction scheduled to begin in the spring of 2026.

Schedule:

Approvals - Complete.
 Design - Complete
 Bidding - Complete
 Construction - 2025 & 2026
 Substantial Completion - 2027

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

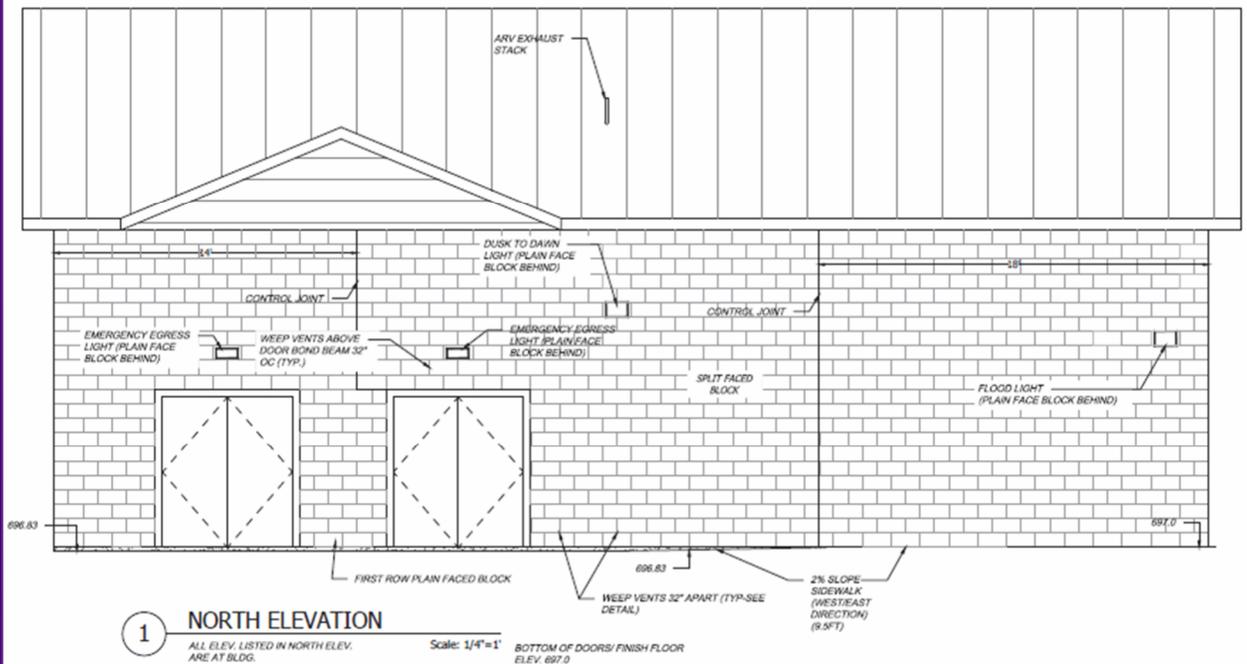

**STATUS
REPORT**

King Lane Community Wells

CIP # 15-002 - King Lane Community Wells

