

CIP # 15-002 - King Lane Community Wells

Project Description:

The project has three primary components: a Pumpouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- ◇ Underground plumbing has been installed and awaiting pressure testing.
- ◇ Interior concrete and masonry scheduled for August.

Schedule:

Approvals - Complete.

Design - Complete


Bidding - Complete

Construction - Started April 2026

Substantial Completion - Scheduled for 12/9/2026

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

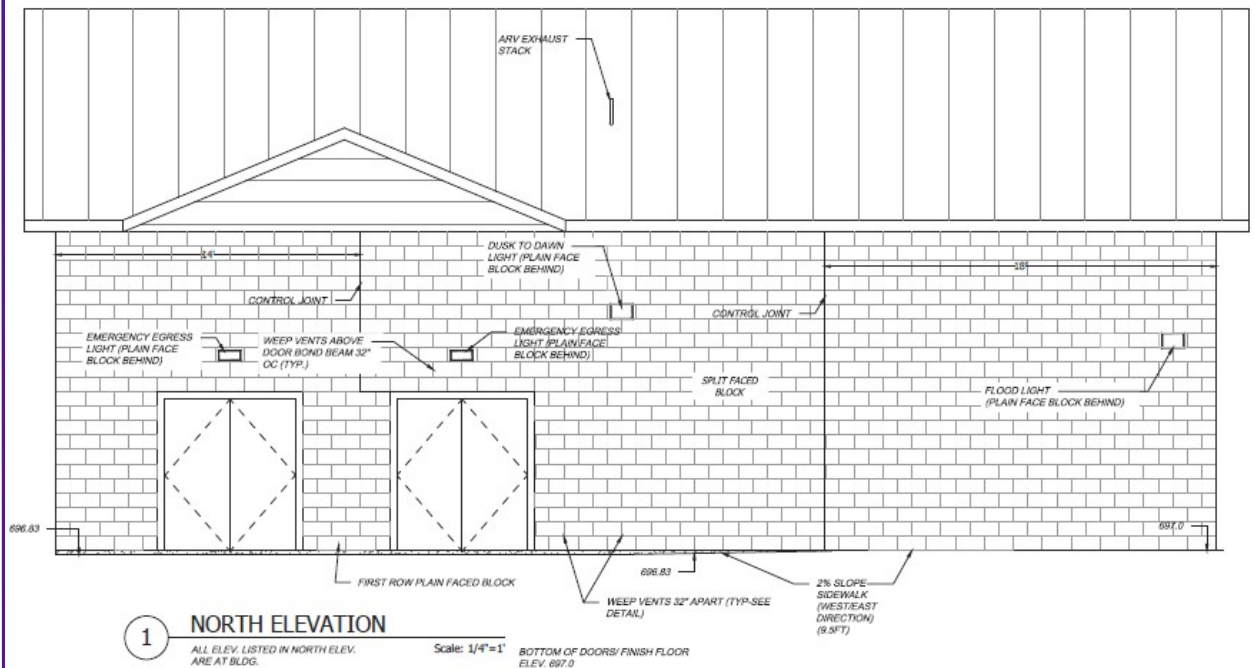

**STATUS
REPORT**

King Lane Community Wells

CIP # 15-002 - King Lane Community Wells

