

CIP # 15-002 - King Lane Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- ◇ Interior concrete is complete.
- ◇ Masonry has begun.
- ◇ New filter vessel has been placed in building

Schedule:

Approvals - Complete.

Design - Complete


Bidding - Complete

Construction - Started April 2026

Substantial Completion - Scheduled for 12/9/2026

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

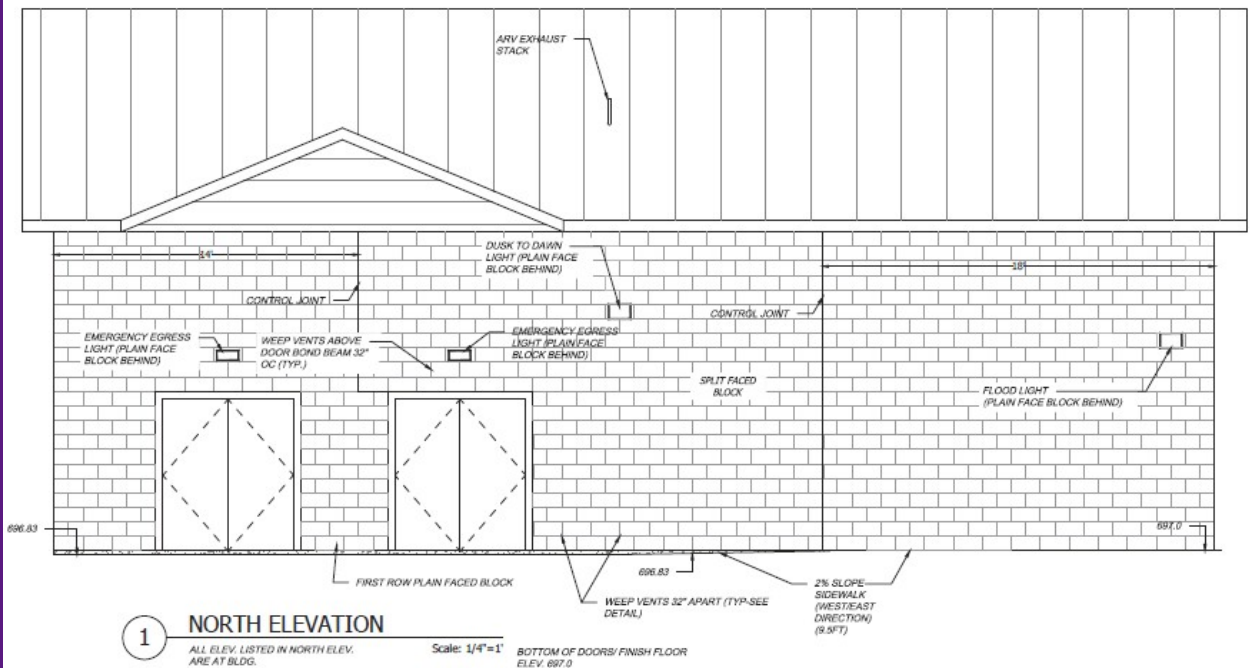

**STATUS
REPORT**

King Lane Community Wells

CIP # 15-002 - King Lane Community Wells



**STATUS
REPORT**

King Lane Community Wells

CIP # 15-002 - King Lane Community Wells

