

ENG# 21-103 - OCHD Isolation Rooms


Project Description:

The project involves modifying the existing HVAC system and associated finishes/systems in two buildings to create isolation (negative pressure) rooms. The Design/Build Contract will include work within the Anna John Resident Centered Care Community (AJRCCC), where three isolation rooms will be created; and work within the Oneida Community Health Center (OCHC) where one isolation room will be created.


Current Status:

Construction activities are complete for the both the AJRCCC & OCHC Isolation Rooms. Currently awaiting Inspection approval from the Department of Health Services for the AJRCCC renovation.

AJRCCC Isolation Room

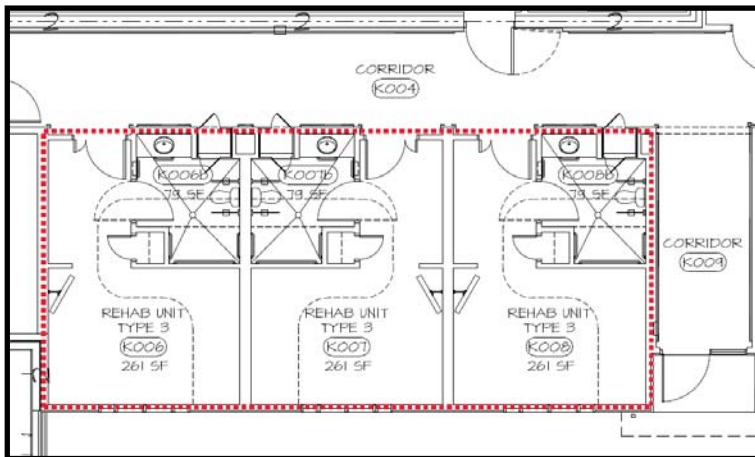

OCHC Isolation Room

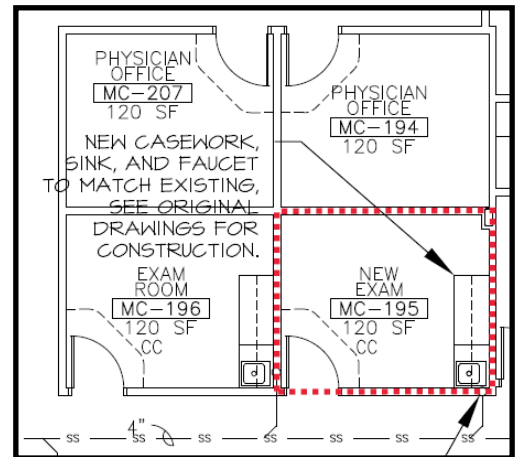

Schedule:

- Approvals - Complete
- Bidding- Complete
- Design - In process
- Construction - In progress
- Substantial Completion:
 - ◆ OCHC—late March 2022
 - ◆ AJRCCC—Early May 2022

Project Partners:

Engineering, OCHD, Purchasing, Legal Office, Mission Support Services.



Oneida Engineering
Department

STATUS
REPORT

ENG# 21-103 - OCHD Isolation Rooms

PROJECT PHOTOS:

AJRCCC Isolation Room

OCHD Isolation Rooms



Oneida Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 5/5/22
