

ENG# 22-104 - Skenandoah Complex Renovation

Project Description:


The project involves remodeling two existing spaces (U012 & U018) within the Skenandoah Complex to functional office spaces. These renovations are needed to better accommodate employee operations. Mission Supports Services (MS2) is the General Contractor (G.C.) for this project.

Renovations to existing room U018 are completed in October 2022.

Current Status:

- ◆ The Task Order for the U012 HR Storage room re-model was issued to G.C. on 1/12/23.
- ◆ Construction activity is scheduled for the week of February 27th, starting with demo activities.
- ◆ Office furniture has been ordered and scheduled for delivery in early April.

Renovation plan to U012 HRD Storage:

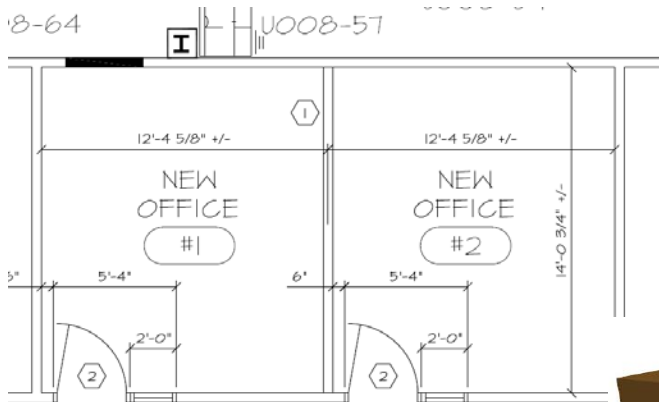

Schedule:

- Approvals - Complete
- Bidding - Complete
- Construction - In progress week of 2/27/23

Project Partners:

Engineering, DPW, Purchasing, Legal Office, HRD, DTS & Mission Support Services, LLC.



Oneida Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 2/23/23
