CIP # 15-002 - Oneida Community Wells

Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- New wells have been installed.
- The pumphouse and water main extension are currently being designed by Indian Health Service (IHS).
 After a tour of a similar facility, it has been decided to revise the design to provide better functionality.
- GEI Consultants are coordinating structural design services and geotechnical investigations with IHS.


Schedule:

•

Approvals - complete. Design - IHS anticipates completion of design in fall 2023. Bidding - 2023 Construction - 2024-2025 Substantial Completion - 2025

Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

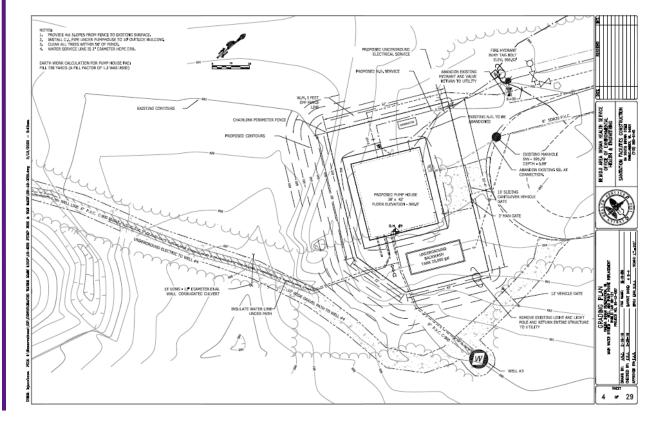

ONEIDA Engineering Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA
