# CIP # 15-002 - Oneida Community Wells

#### **Project Description:**

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

### **Current Status:**

- New wells have been installed.
- The pumphouse and water main extension are currently being designed by Indian Health Service (IHS).
  - ♦ After a tour of a similar facility, it has been decided to revise the design to provide better functionality.
- Geotechnical field work complete, currently analyzing data collected.

#### Schedule:

Approvals - complete.


Design - IHS anticipates completion of design in fall 2023.

Bidding - 2023

Construction - 2024-2025 Substantial Completion - 2025

## **Project Partners:**

Utilities Dept., Land Management, Engineering, DPW, IHS

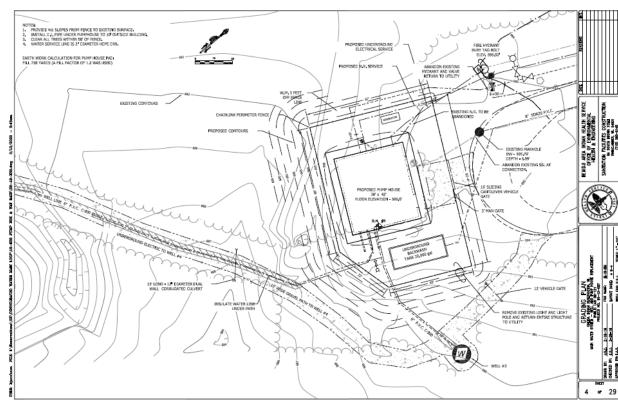

Date: 7/27/23

