

## ENG# 23-111 - Skenandoah Complex Lobby Renovation

### Project Description:


The purpose of this project is to remodel the Skenandoah Complex lobby area to create a safer and more secure working environment for employees along with providing added measures to restrict access into the secure areas of the building. Additionally, the remodel includes a new restroom to eliminate guest from utilizing the employee restrooms.

Per OBC Resolution #04-08-20-K, the Engineering Department will be contracting with Mission Support Services, LLC for Design-Build services.

### Current Status:

Demolition activities commenced on 6/25. Project is continuing with scheduled activities.

## Skenandoah Complex Lobby Renovation

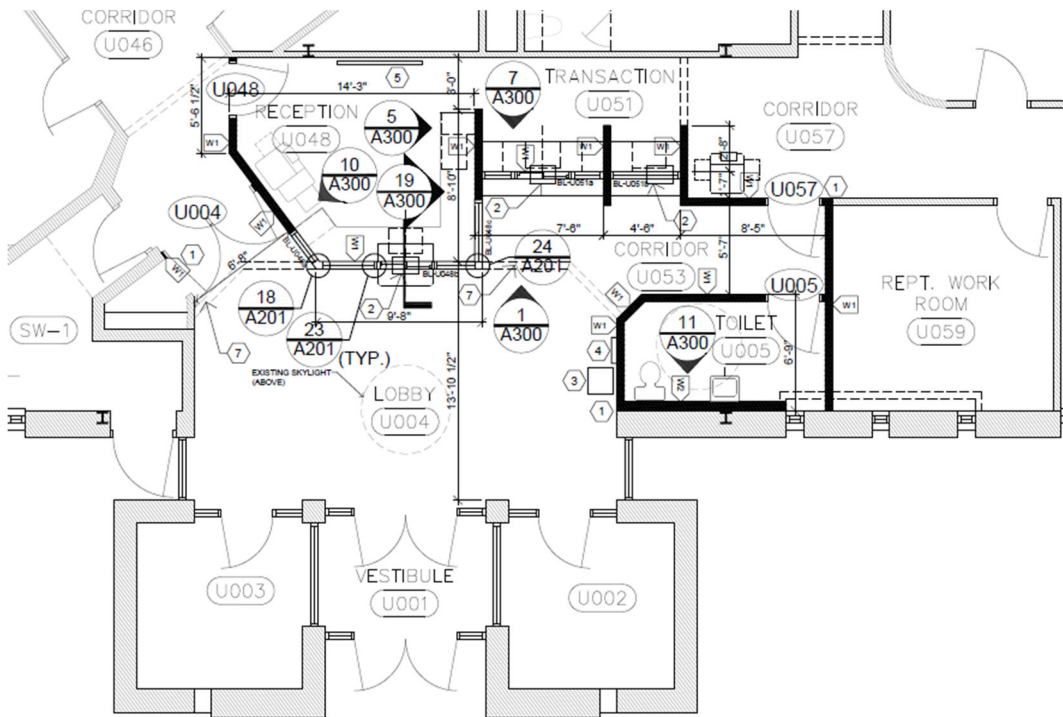

### Schedule:

Approvals - Complete  
Design - Complete  
Construction - In progress  
Substantial Completion – mid- September 24'

### Project Partners:

Engineering, HRD, DPW, Accounting, Licensing, Purchasing, DTS, Legal Office.



Oneida Engineering  
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 6/27/24

**STATUS  
REPORT**

**ENG# 23-111 - Skenandoah Complex Lobby Renovation**

**PROGRESS PHOTOS:**



**Skenandoah Complex  
Lobby Renovation**



Oneida Engineering  
Department

*DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA*

**Date: 6/27/24**
