

ENG# 23-111 - Skenandoah Complex Lobby Renovation

Project Description:


The purpose of this project is to remodel the Skenandoah Complex lobby area to create a safer and more secure working environment for employees along with providing added measures to restrict access into the secure areas of the building. Additionally, the remodel includes a new restroom to eliminate guest from utilizing the employee restrooms.

Per OBC Resolution #04-08-20-K, the Engineering Department will be contracting with Mission Support Services, LLC for Design-Build services.

Current Status:

Current activities consist of: flooring removal, installing ceiling grid/ tile, electrical finishes, HVAC mods and installing tile within restroom. Project is continuing with scheduled activities as necessary.

**Skenandoah Complex
Lobby Renovation**

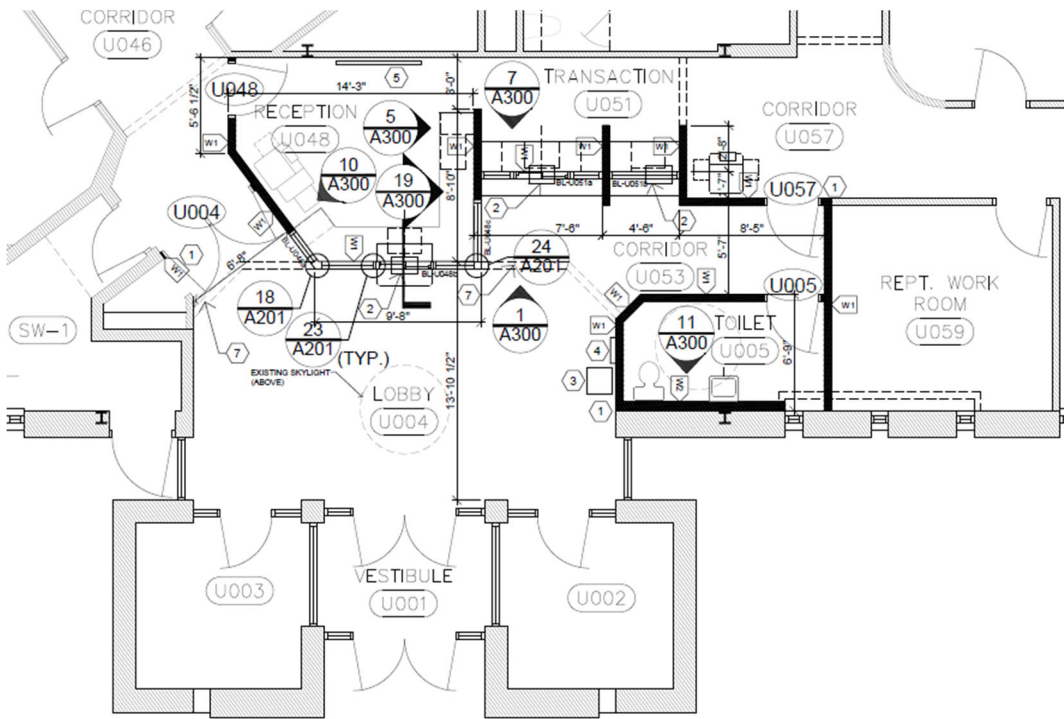

Schedule:

- Approvals - Complete
- Design - Complete
- Construction - In progress
- Substantial Completion – mid- September 24'

Project Partners:

Engineering, HRD, DPW, Accounting, Licensing, Purchasing, DTS, Legal Office.



Oneida Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 8/2/24

**STATUS
REPORT**

ENG# 23-111 - Skenandoah Complex Lobby Renovation

PROGRESS PHOTOS:



**Skenandoah Complex
Lobby Renovation**



Oneida Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 8/2/24
