

# CIP # 15-002 - Oneida Community Wells

## Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

## Current Status:


- New wells have been installed.
- Project bidding came back over budget.
- IHS is in the process of redesigning to bring project costs down.

## Schedule:

Approvals - complete.  
 Design - complete  
 Bidding - 2025  
 Construction - 2025  
 Substantial Completion - 2027

## Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

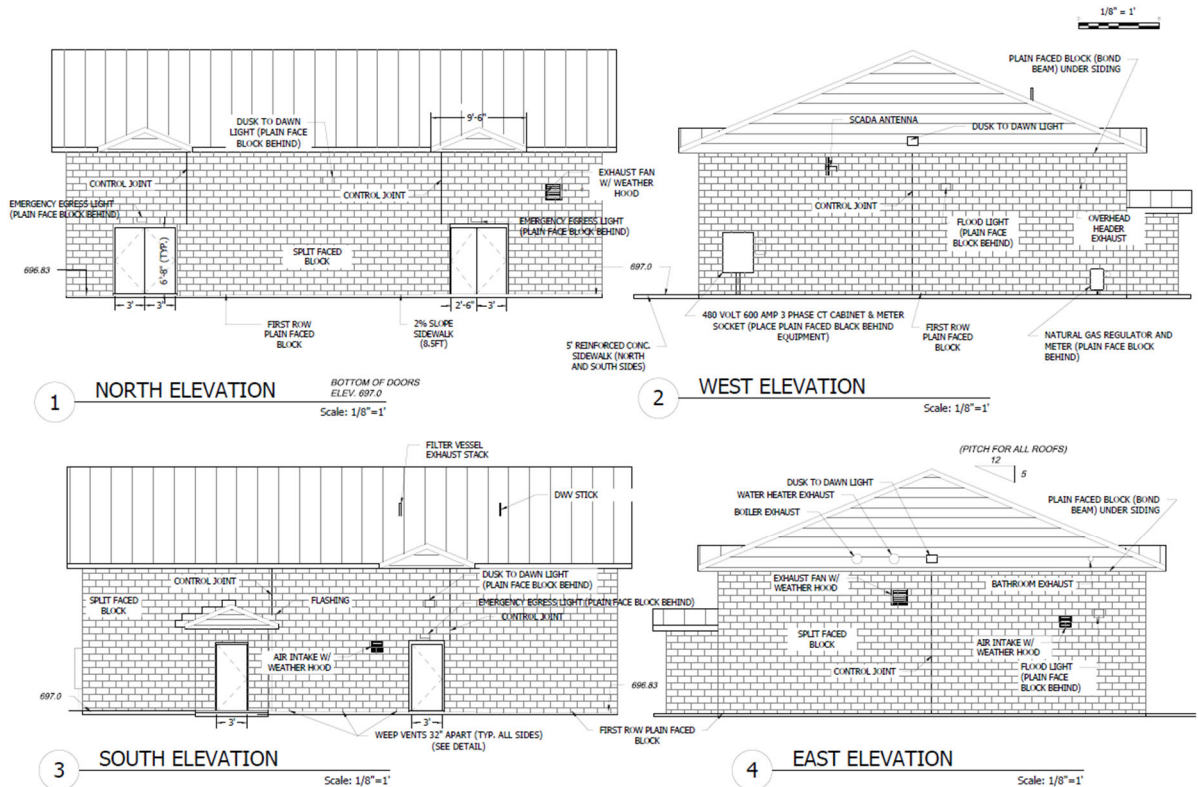

# CIP # 15-002 - Oneida Community Wells

