

# CIP # 15-002 - Oneida Community Wells

## Project Description:

The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

## Current Status:


- Project will be rebid for 2 separate contracts.
  - ◊ Phase One - Watermain Work is out for bid.
  - ◊ Phase Two - Pumphouse scheduled for bidding in March 2025.

## Schedule:

Approvals - complete.  
 Design - complete  
 Bidding - 2025  
 Construction - 2025 & 2026  
 Substantial Completion - 2027

## Project Partners:

Utilities Dept., Land Management, Engineering, DPW, IHS

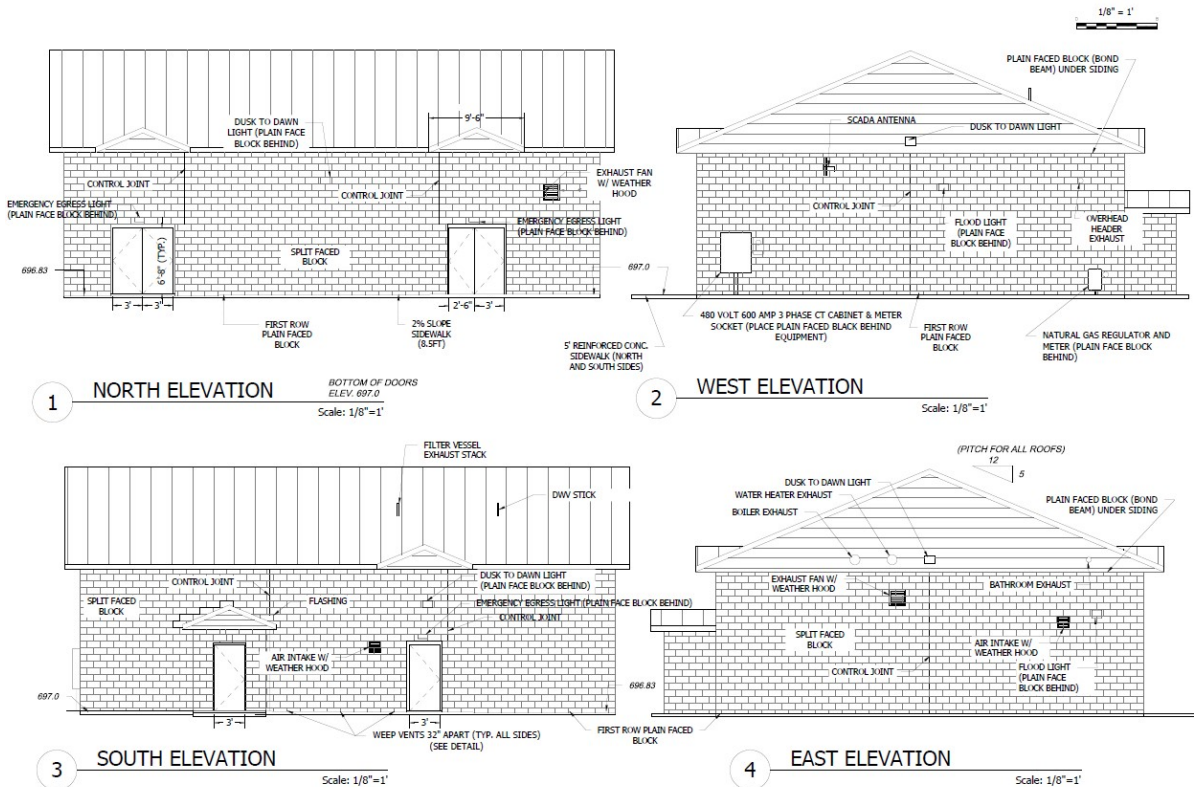

**STATUS  
REPORT**

**Oneida Community Wells**

**CIP # 15-002 - Oneida Community Wells**

