

## CDC# 23-116 –Rolling Hills Water Tower Replacement

**Project Description:**

The project will replace the exist water tower located in the Rolling Hills Subdivision. The new tower is needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

**Current Status:**


- Foundation installation complete.
- Steel scheduled for delivery and erection in March 2026.
- Watermain phase on Seminary Road and King Lane will be complete in February.

**Schedule:**

Approvals - Completed  
Design - Completed  
Bidding - Completed  
Construction - Ongoing  
Substantial Completion - 2026

**Project Partners:**

DPW, Engineering, Planning

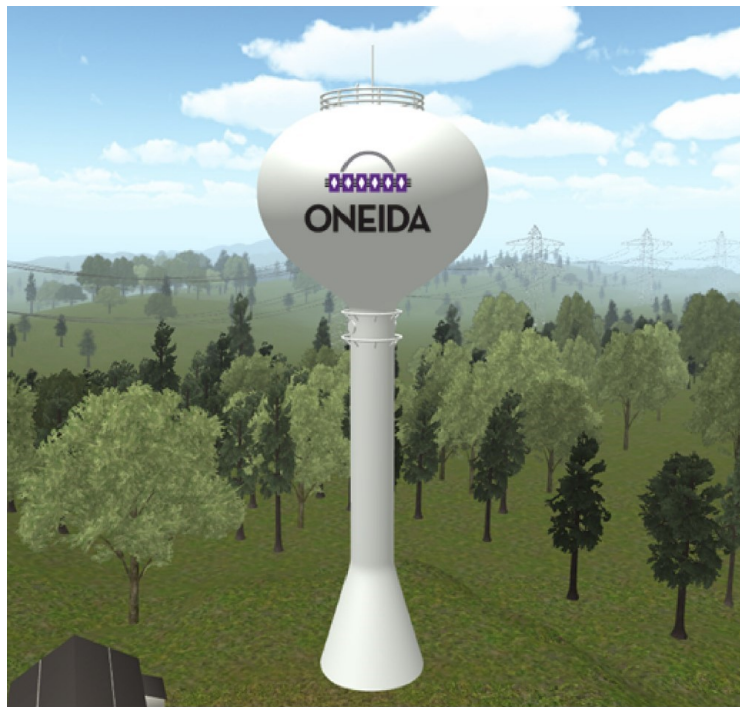

## STATUS REPORT

# Rolling Hills Water Tower

## CDC# 23-116 –Rolling Hills Water Tower Replacement



Engineering  
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

**Date: 2/4/2026**
