

CIP # 20-101 - Museum Relocation

Project Description:

The project proposes to relocate the existing museum to a more accessible and identifiable location at 760 Airport Road (Hwy 172). The existing building on the property will be renovated to accommodate the functional and environmental (*heating, cooling, humidity control, infestation prevention, etc.*) needs of the Oneida Museum.

Current Status:

- Interior finishes are in progress.
- Exterior concrete and landscaping scheduled for spring.
- The Exhibits team has begun installation of gallery items.
- Grand Opening Scheduled for June 20, 2026

Schedule:

Approvals - Completed

Concept Design - Completed

Final Design, Engineering & Bidding - Completed

Construction - Underway

Substantial Completion - 2026

Project Partners:


Museum, GSD, Cultural Heritage, Engineering, DPW, DTS



**STATUS
REPORT**

CIP # 20-101 - Museum Relocation

Museum Relocation

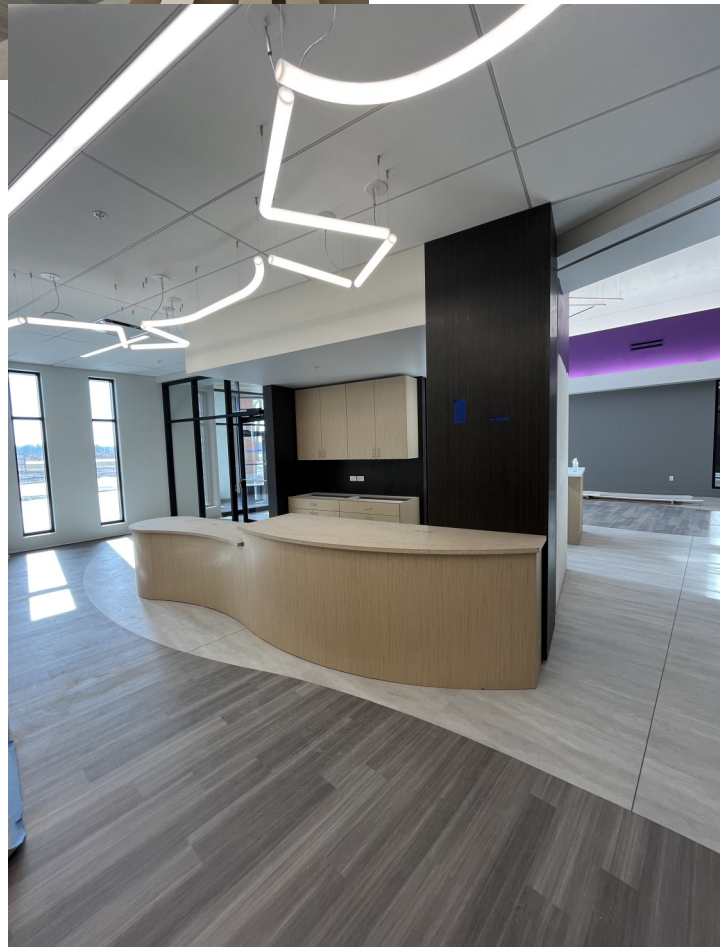

**STATUS
REPORT**

CIP # 20-101 - Museum Relocation

Museum Relocation



Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 4/2/2026
