

CIP# 23-113—Oneida Judicial Center - Safety Upgrades

Project Description:

The project will create a new secure public entrance area to the building allowing the security team to prescreen all visitors before they gain access to the inside.

Current Status:


- Construction has begun.
 - ◊ Temporary public entrance has moved to front/south side of building.
- Demo, excavation, foundations and structural steel installation are complete.
- Framing and rough in work scheduled for July.

Schedule:

- Approvals - Completed
- Concept Design - Completed
- Final Design - Completed
- Construction - Scheduled to start spring of 2026
- Substantial Completion - September 2026

Project Partners:

Oneida Judiciary, Security, Engineering, Planning, DPW, DTS

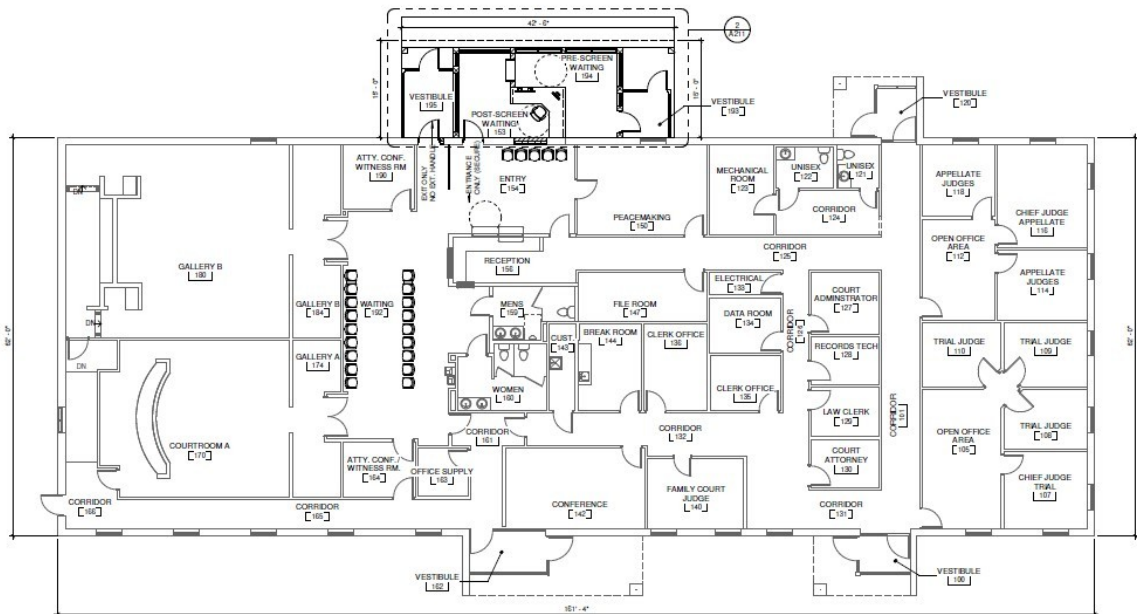

**STATUS
REPORT**

CIP# 23-113—Oneida Judicial Center - Safety Upgrades

OJC Safety Upgrades



ONEIDA Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 7/1/2026
