

CIP# 23-113—Oneida Judicial Center - Safety Upgrades

Project Description:

The project will create a new secure public entrance area to the building allowing the security team to prescreen all visitors before they gain access to the inside.

Current Status:


- Framing is complete.
- Rough-ins for electrical plumbing and heating has started.
- Roofing to be installed early August.
- Interior finishes scheduled for August.

Schedule:

Approvals - Completed
 Concept Design - Completed
 Final Design - Completed
 Construction - Scheduled to start spring of 2026
 Substantial Completion - September 2026

Project Partners:

Oneida Judiciary, Security, Engineering, Planning, DPW, DTS

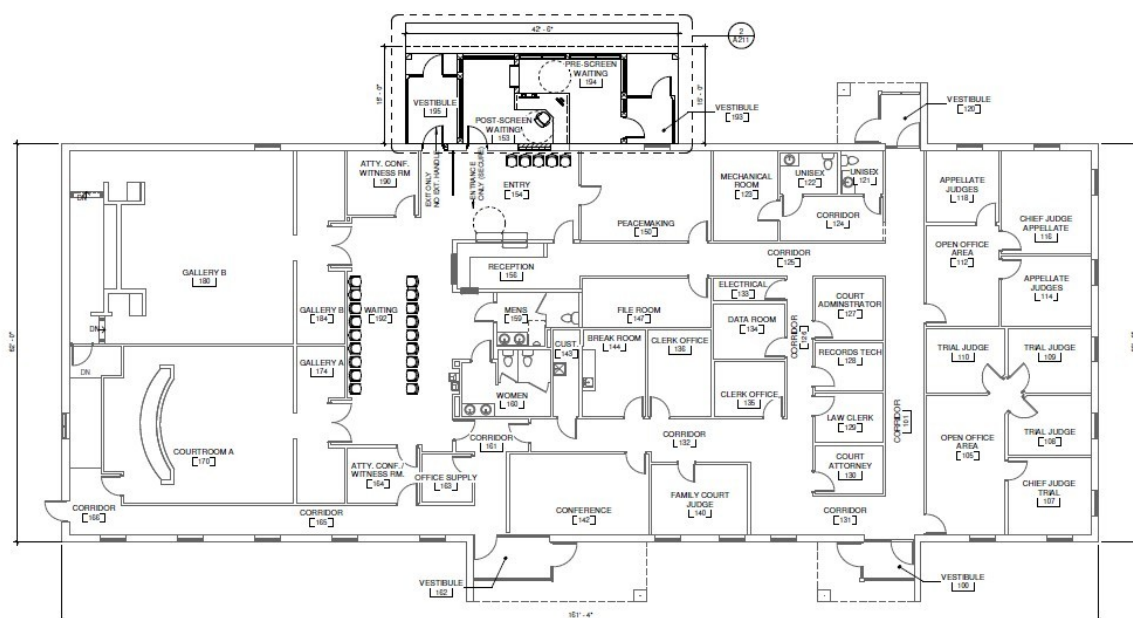

**STATUS
REPORT**

OJC Safety Upgrades

**CIP# 23-113—Oneida Judicial Center -
Safety Upgrades**

