

## **CIP # 21-111 — Multi-Family Housing**

### **Project Description:**

The project would develop multi-family residential units (apartments) to address the housing needs of the Oneida Community that are currently not offered or are in limited supply. The project will develop a total of 18 apartment units with a mixture of two and three bedroom units. The units will be managed by Comprehensive Housing Division.

### **Current Status:**

- Re-Zoning - complete 2/13/23.
- Wetlands - Wetland Mitigation Credits have been purchased.
- Design - Waiting on MS2 to provide pricing.
- Design - Working with Focus on Energy on energy efficiency items.

### **Schedule:**

Approvals - complete 7/27/22

Design - 10/2022– 09/2023

Construction - 10/2023 - 12/2024

Substantial Completion - 11/2024



### **Project Partners:**

Engineering, Comprehensive Housing, DPW



# CIP # 21-111 — Multi-Family Housing

## Multi-Family Housing

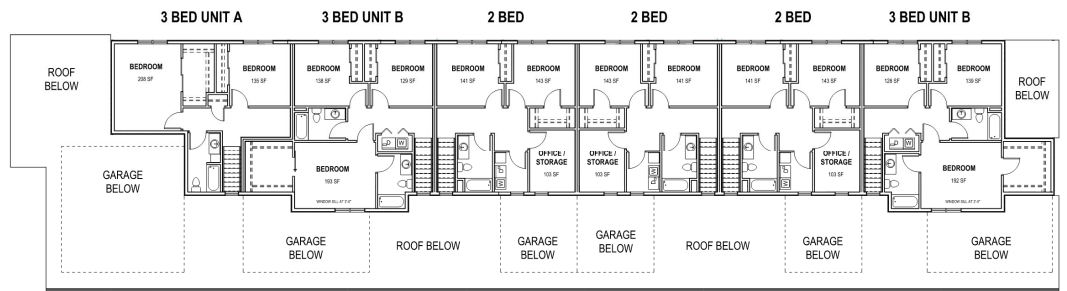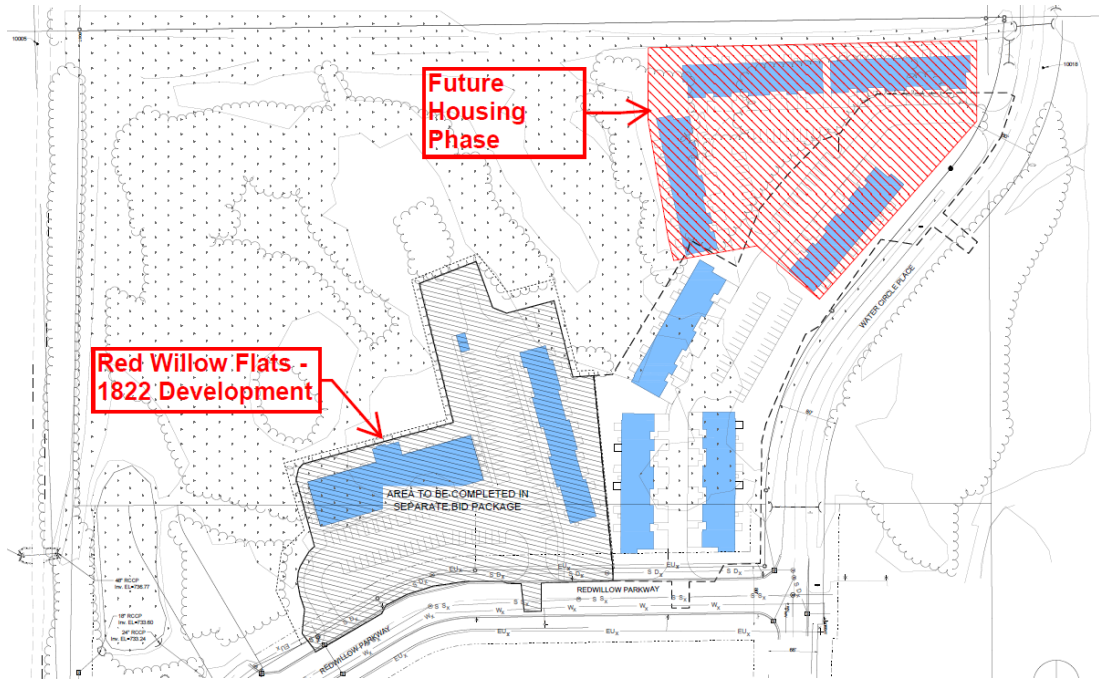

② 6 UNIT LAYOUT - SECOND FLOOR  
1/8" = 1'-0"

