

**CDC #22-108-Veterans Memorial Improvements**

**Project Description:**


To correspond with the park’s Site Amenities project, this proposed Veterans Memorial Improvements Project will include improved parking, new sidewalks, improved lighting and various added improvements.

**Current Status:**

- Project is set to begin final work April 1st 2024.
- Vinton Construction completed most of flatwork concrete.
- Vinton installed the binder course of asphalt for parking lot.
- Vinton is targeting a completion of project by end of May 2024.

**Schedule:**

Approvals - 2022  
 Design - 2023  
 Bidding - 2023  
 Construction - 2023-2024  
 Substantial Completion - 2023

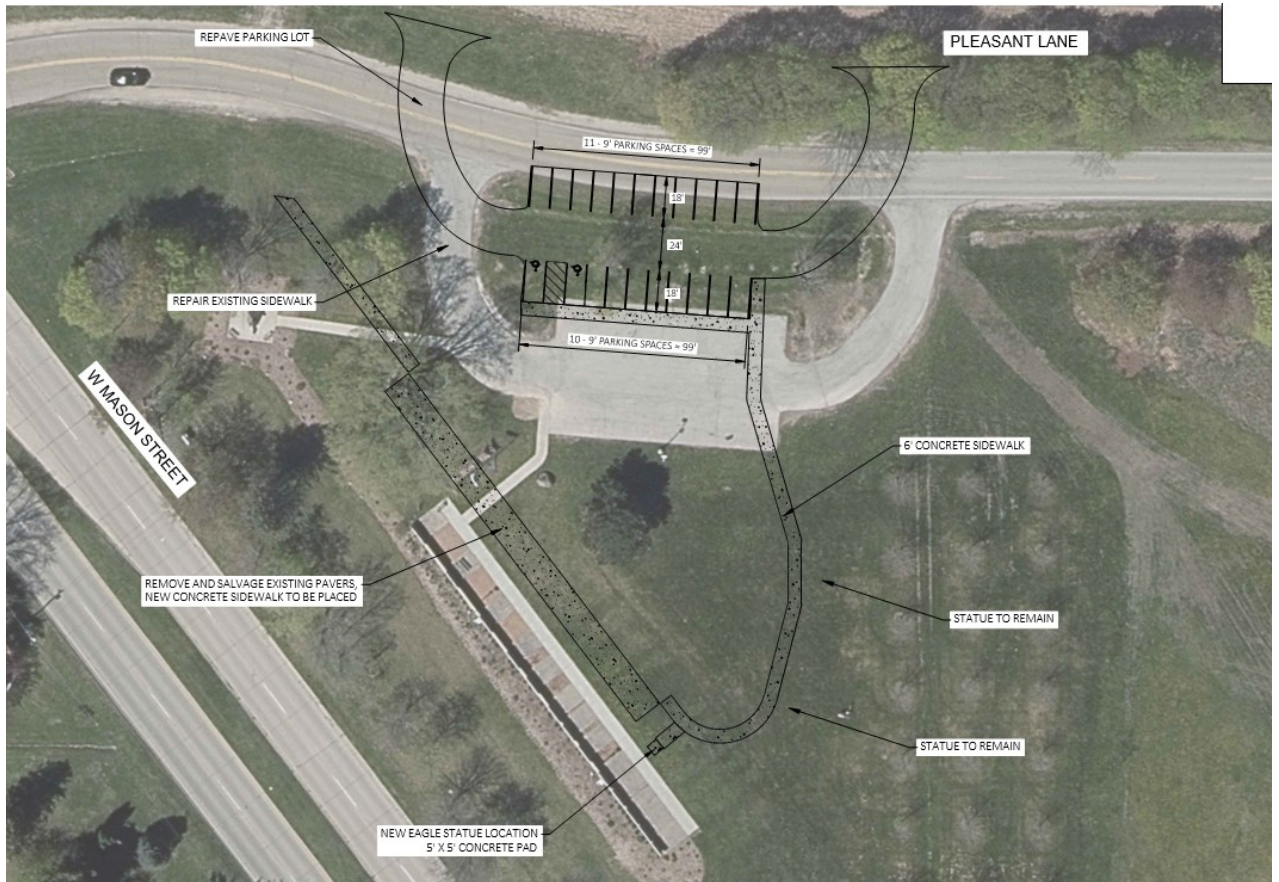



## CDC #22-108-Veterans Memorial Improvements

### Project Description:

To correspond with the park's Site Amenities project, this proposed Veterans Memorial Improvements Project will include improved parking, new sidewalks, improved lighting and various added improvements.

### Current Status:





## CDC #22-108-Veterans Memorial Improvements

### Project Description:

To correspond with the park's Site Amenities project, this proposed Veterans Memorial Improvements Project will include improved parking, new sidewalks, improved lighting and various added improvements.

### Current Status:

- Project is on Pause until Spring of 2024.

