

## **ENG# 22-105 - Mission Park Renovations**

### **Project Description:**

Mission Park is one of (17)- parks on the reservation maintained by the Oneida Parks and Recreation Department. Consideration to upgrade the Nation’s park system creates opportunities for tribal community to connect with the natural environment, improve healthy lifestyles socially, physically, culturally and emotionally. Over the years, surface water resulting from inadequate drainage along with modifications to the park caused stagnant water and maintenance issues which posed problems, preventing its full utilization.

The proposed project is to modify the existing park conditions to a create a more functional recreational area for the Oneida Community. This plan would eliminate frequent maintenance activities and create a more useful park by implementing drainage mitigation measures such as: curb and gutter, asphalt paving and installing storm water drainage pipes to prevent future flooding of the park. Poor draining characteristics within the site have prevented full utilization of the park for decades. Additionally, portions of the outfield fencing will be modified to provide additional protection to the adjacent residential housing. Mission Park is regularly used by the Oneida Nation School system and the Oneida community for various sporting events and recreational activities throughout the year.

### **Current Status:**

The final top-coat of asphalt and pavement markings were completed the week of April 22nd. Once conditions are suitable, Vinton will complete the installation of topsoil and seeding throughout various areas of the project. Project signage will be installed in the coming week(s).

***Refer to next page for various progress photos***

### **Schedule:**

Design - Complete  
Bidding- Complete  
Construction - In process

### **Project Partners:**

Engineering, DPW, Recreation, Purchasing, Legal Office, Oneida Engineering Solutions, Vinton Construction Company




**ONEIDA**

Oneida Engineering  
Department

**STATUS  
REPORT**

**ENG# 22-105 - Mission Park Renovations**

**Progress Photos**

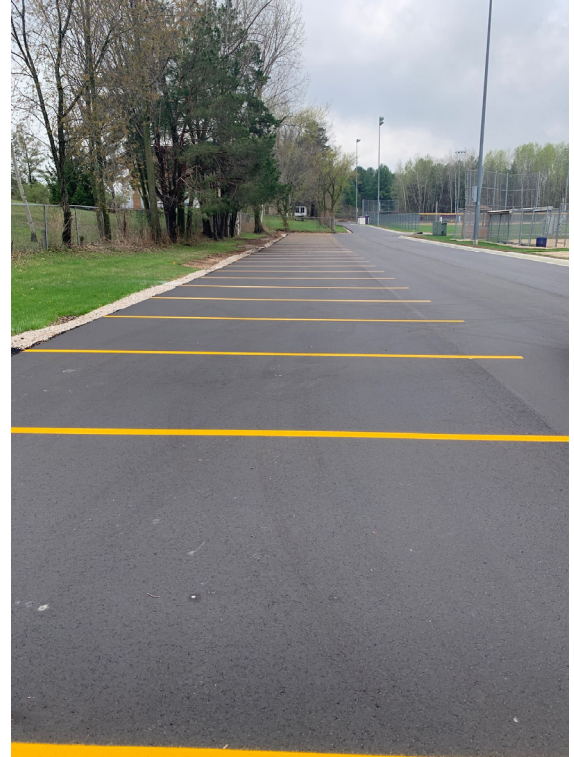

**Mission Park Renovations**



**ONEIDA**

Oneida Engineering  
Department

*DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA*

**Date: 4/30/24**
