CIP # 21-111 — Multi-Family Housing

Project Description:

The project would develop multi-family residential units (apartments) to address the housing needs of the Oneida Community that are currently not offered or are in limited supply. The project will develop a total of 12 apartment units with a mixture of two and three bedroom units. The units will be managed by Comprehensive Housing Division.

Current Status:

- Construction has begun.
 - ♦ Excavation has started.
 - ♦ Foundations planned for middle of July.

Schedule:

Approvals - complete 7/27/22 Design - finished in 2024 Construction - 2024 Substantial Completion - 2025

Project Partners:


Engineering, Comprehensive Housing, DPW



Date: 6/28/2024



CIP # 21-111 — Multi-Family Housing

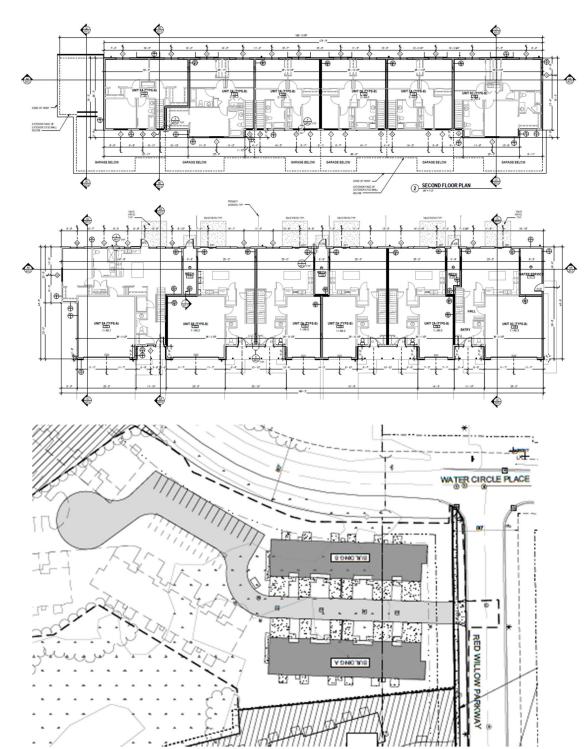

Date: 6/28/2024

