

ENG# 24-102 - Casino Grill-Market Remodel

Project Description:

The purpose of this project is to remodel the existing food court within the Main Casino to provide additional food services. The project includes heated and refrigerated display grab-and go merchandiser's, a staffed grill area, production/ storage spaces, liquor storage along with customer seating.

The Nation has contracted with the following vendors and services:

- ◇ Bergman Walls & Associates (BWA) - Construction Documents
- ◇ Camera Corner Connecting Point - Food Court Displays, Controls, Devices & Hardware
- ◇ Faith Technologies - Network Cabling
- ◇ TSI—Surveillance Materials
- ◇ Mission Support Services –General Contractor.

Additionally, Gaming is utilizing OVG Hospitality to assist with preliminary design and Kitchen equipment

Current Status:

Construction activities are in progress. Current activities consist of: framing, MEP rough-ins & sheetrock installations. The new and existing kitchen equipment have been delivered to the project site. Various pieces of equipment have been installed.

Refer to Page 2 for Progress Photos

Schedule:

Approvals - On-Going
Design - Complete
Construction - In Progress
Substantial Completion – End of September 2024

Project Partners:

Engineering, Gaming, OVG, EHSLA, Zoning, DTS, Surveillance, Legal Office.




Oneida Engineering
Department

STATUS
REPORT

ENG# 24-102 - Casino Grill-Market Remodel

Progress Photos:

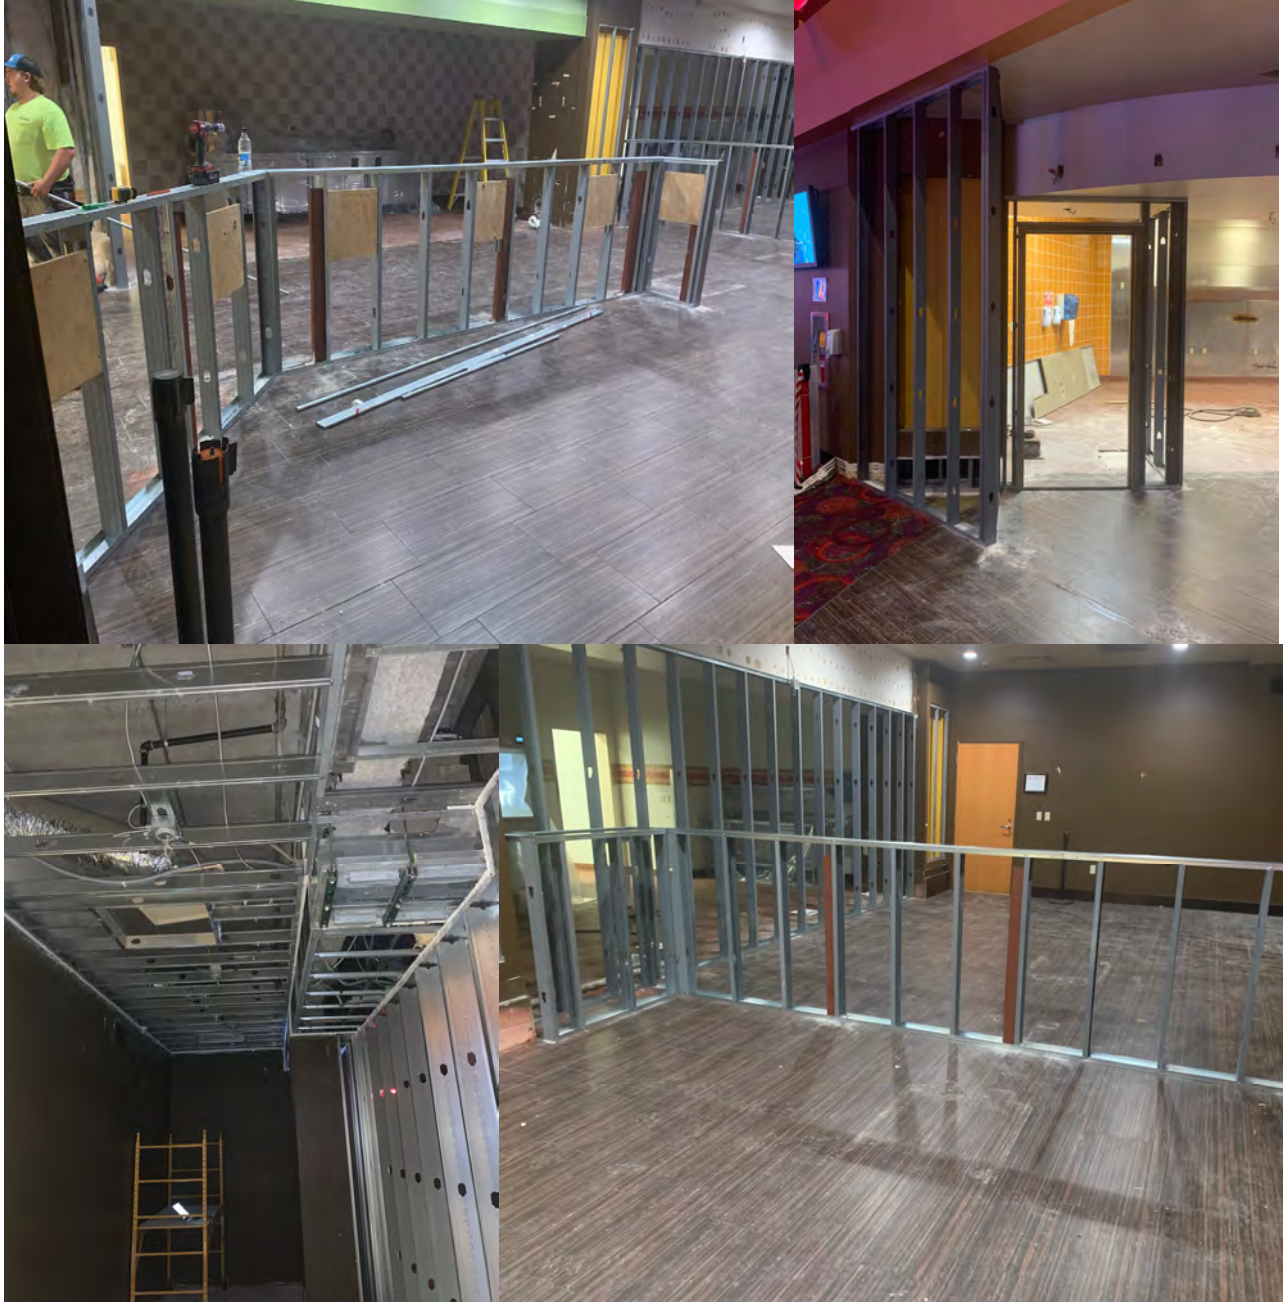

Casino Grill-Market Remodel



Oneida Engineering
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 8/2/24
