

# Oneida Community Cannery

## STATUS REPORT

### CIP # 15-001 Oneida Community Cannery

#### **Project Description:**

The proposed Oneida Community Cannery (formerly named Food Innovation Center) would develop a new facility for the Oneida Nation Cannery and its programmatic efforts. The purpose of this project is to focus this center to be a new cannery and training facility. The Community Cannery will allow for the Cannery to best serve the community and the demand placed on the program by facilitating the food processing needs of the community, and continuing to allow for the transfer of knowledge of food and empowering our citizens in the safe production and processing of their own foods.

#### **Current Status:**

- Milbach Construction Services is the General Contractor for the Cannery Project.
- Pre-Engineered Metal Building is erected with roof and sidewall metal yet to install.
- Plumbing rough-ins are completed.

#### **Schedule:**

Approvals - 2022

Design - 2023-2025


Bidding - 2025

Construction - 2025-2026

Substantial Completion - June 2026

#### **Project Partners:**

Environmental, Land & Agriculture Division - Food & Agriculture Area; Engineering Dept., DPW—Facilities

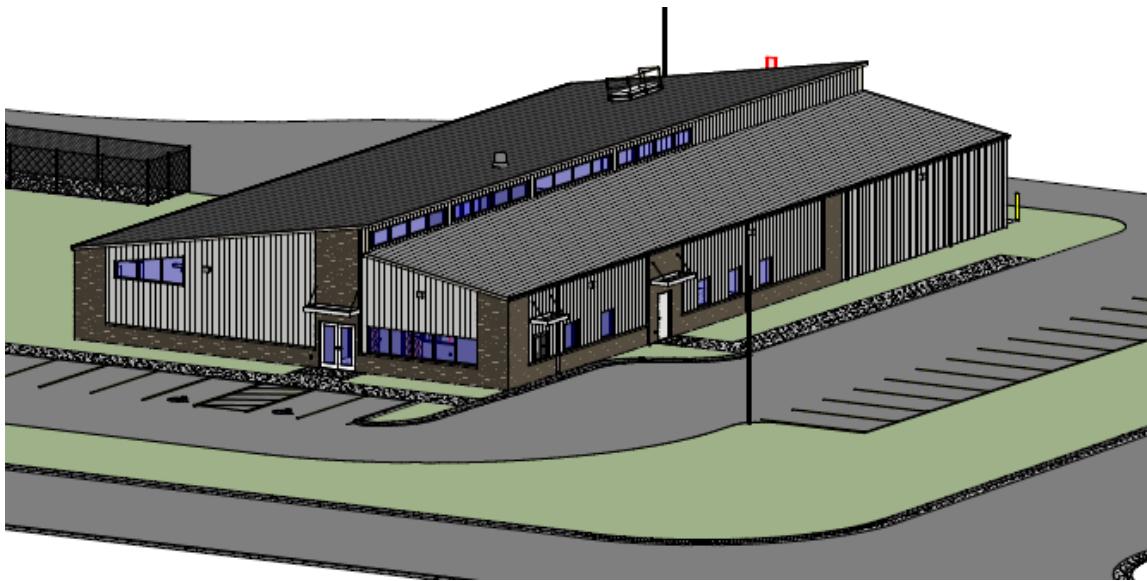

Conceptual Exterior



Engineering  
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

**Date: 1/05/26**

# Oneida Community Cannery

STATUS  
REPORT

## CIP # 15-001 Oneida Community Cannery



Engineering  
Department

DEVELOPING A COMMUNITY OF WELL-BEING THAT IS UNIQUELY ONEIDA

Date: 1/05/26
