STATUS REPORT

OJC Safety Upgrades

CIP# 23-113—Oneida Judicial Center - Safety Upgrades

Project Description:

The project will create a new secure public entrance area to the building allowing the security team to prescreen all visitors before they gain access to the inside. The project will also install a new secure privacy fenced in area for Judiciary staff to parking including more dedicated staff parking spaces.

Current Status:

- Construction to begin at end of May.
    - ◊ Temporary public entrance will be moved to froint of building starting June 1.

Schedule:

Approvals - Completed
Concept Design - Completed
Final Design - Completed
Construction - Scheduled to start spring of 2026
Substantial Completion - September 2026

Project Partners:

Oneida Judiciary, Security, Engineering, Planning, DPW, DTS

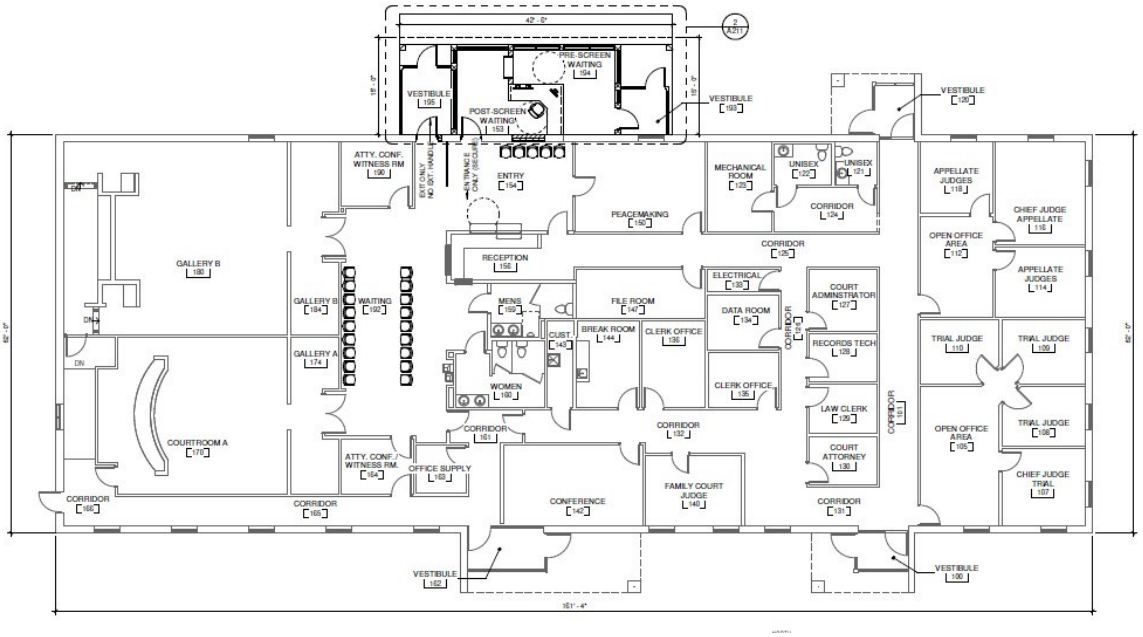

ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 5/6/2026
