STATUS REPORT

OJC Safety Upgrades

# CIP# 23-113—Oneida Judicial Center - Safety Upgrades

## Project Description:

The project will create a new secure public entrance area to the building allowing the security team to prescreen all visitors before they gain access to the inside.

## Current Status:

- Construction has begun.
  - ◊ Temporary public entrance has moved to front/south side of building.
- Demo, excavation and foundations scheduled for June.

## Schedule:

Approvals - Completed
Concept Design - Completed
Final Design - Completed
Construction - Scheduled to start spring of 2026
Substantial Completion - September 2026

## Project Partners:

Oneida Judiciary, Security, Engineering, Planning, DPW, DTS

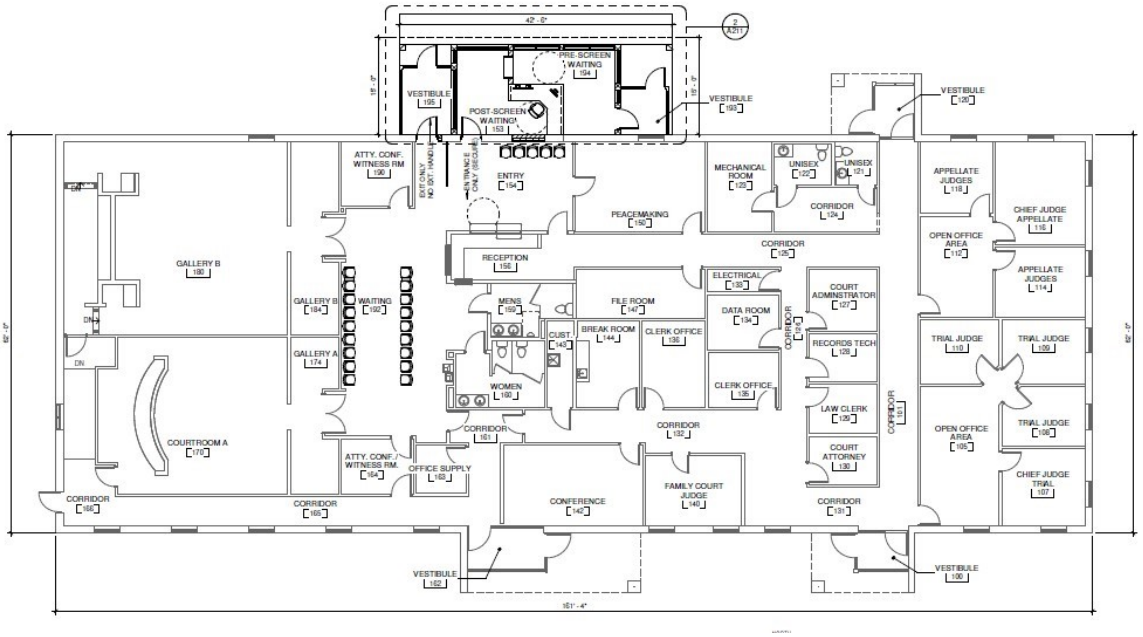


ONEIDA Engineering Department

*Developing a Community of Well-Being that is Uniquely Oneida*

**Date: 6/1/2026**
