STATUS REPORT

Rolling Hills Water Tower

CDC# 23-116 –Rolling Hills Water Tower Replacement

Project Description:
The project will replace the exist water tower located in the Rolling Hills Subdivision. The new tower is needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- Tower erection is complete.
- Painting and interior coating are complete.
    - ◊ Logo to be painted on in July.

Schedule:
Approvals - Completed
Design - Completed
Bidding - Completed
Construction - Ongoing
Substantial Completion - 2026

Project Partners:
DPW, Engineering, Planning

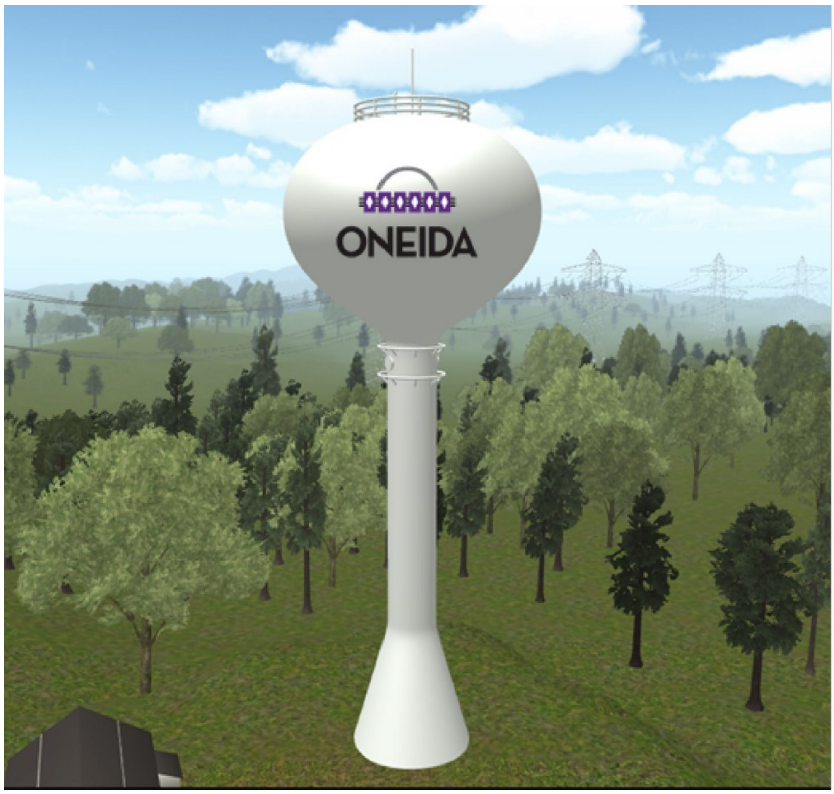

ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 7/1/2026

STATUS REPORT

Rollihng Hills Water Tower

CDC# 23-116 –Rolling Hills Water Tower Replacement

ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 7/1/2026
