STATUS REPORT

King Lane Community Wells

CIP # 15-002 - King Lane Community Wells


Project Description:
The project has three primary components: a Pumphouse, Water Main Extension, and new high capacity wells. These components are needed to address identified deficiencies in the water system noted in the *Master Plan for the Oneida Community Water System* prepared by Indian Health Service (IHS).

Current Status:

- ◊ Masonry work complete and roof trusses have been installed.
- ◊ Interior painting in progress.
- ◊ Underground pipe work in progress.

Schedule:
Approvals - Complete.
Design - Complete
Bidding - Compete
Construction - Started April 2026
Substantial Completion - Scheduled for 12/9/2026

Project Partners:
Utilities Dept., Land Management, Engineering, DPW, IHS

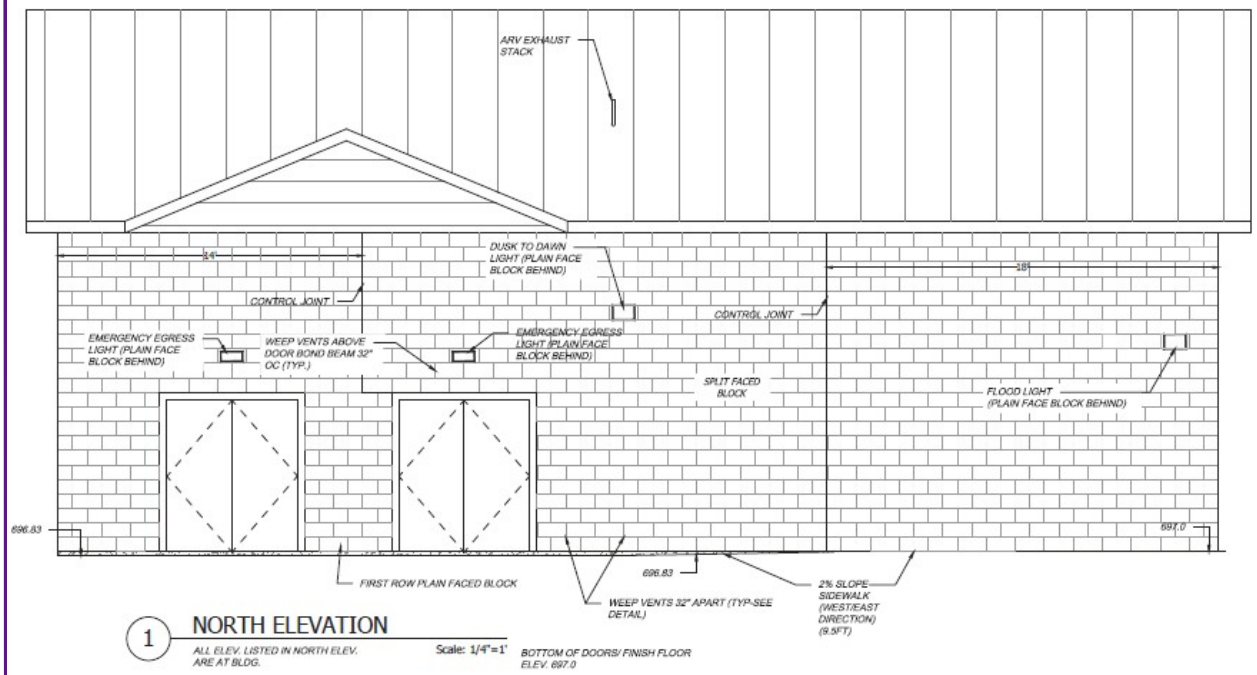

ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 10/30/2026

STATUS REPORT

CIP # 15-002 - King Lane Community Wells

King Lane Community Wells





ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 10/30/2026

STATUS REPORT

CIP # 15-002 - King Lane Community Wells





King Lane Community Wells

ONEIDA Engineering Department

Developing a Community of Well-Being that is Uniquely Oneida

Date: 10/30/2026
